

Piedmont Park Boardwalk, Dock, and Road/Trail Improvements



DPR with the Moving Atlanta Forward Social Bond 2022-A1 is performing major renovations and improvements of the existing boardwalk, dock and roadways/trails.

Planning/Scoping	Engineering/Design	Procurement	Construction	Closeout
100%	100%	100%	95%	0%

LOCATION


Address: 400 Park Dr. NE
Council District: 6
Classification: Regional

PROJECT DETAILS

Manager: Keith Hicks
Number: 400127-22 & 44
Overall Budget: \$875,000

TIMELINE (Last Updated: April 2024)

Planning/Scoping: March 2023
Engineering/Design: March 2023
Procurement: April 2023
Construction: July 2023
Closeout: May 2024
Projected Completion Date: June 2024
Project Duration: 15 months

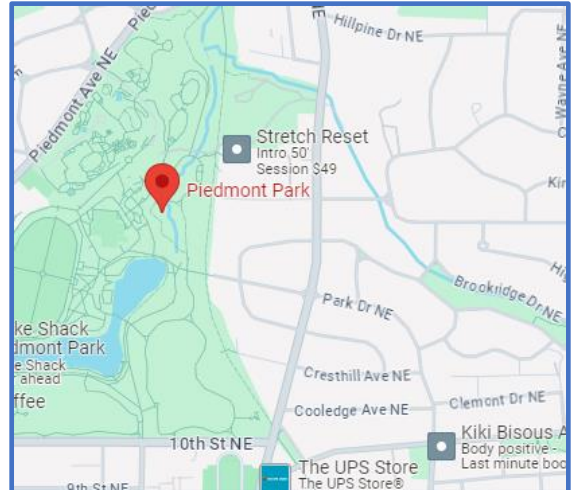

ENCUMBERED FUNDING

FUND	FY23	FY24	FY25
3163-MAF Social Bond 2022-A1	\$829,437		

(Last Updated: May 2024)

Olmstead Park Improvements



DPR with the Moving Atlanta Forward Social Bond 2022-A1 will install drainage improvements, repave asphalt and add signage.

Planning/Scoping	Engineering/Design	Procurement	Construction	Closeout
100%	100%	100%	0%	0%

LOCATION


Address: 1788 Ponce De Leon
Council District: 6
Classification: Neighborhood

PROJECT DETAILS

Manager: Fred Cartwright
Number: 400127-28
Overall Budget: \$400,000

TIMELINE

Planning/Scoping: June 2023
Engineering/Design: July 2023
Procurement: March 2024
Construction: April 2024
Closeout: October 2024
Projected Completion Date: December 2024
Project Duration: 18 Months

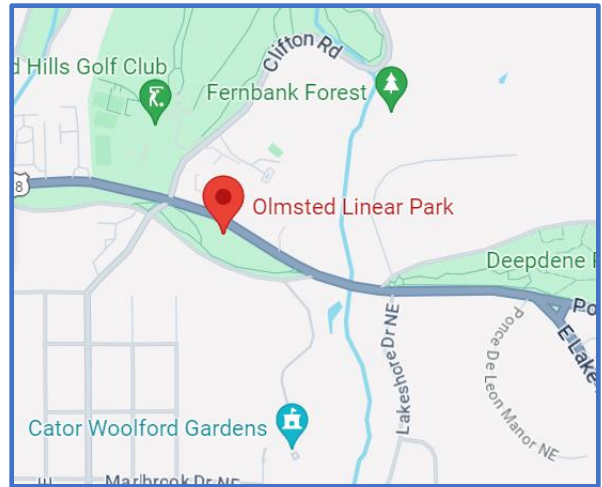

ENCUMBERED FUNDING

FUND	FY23	FY24	FY25
3163-MAF Social Bond 2022-A1	\$279,026		

Morningside Nature Preserve



DPR with the Moving Atlanta Forward Social Bond 2022-A1 will...Parking lot refresh, ADA Parking spaces, bridge replacement, trail improvements and boardwalk repair.

Planning/Scoping	Engineering/Design	Procurement	Construction	Closeout
100%	100%	100%	25%	0%

LOCATION


Address: 2020 Lenox Rd. NE
Council District: 6
Classification: Nature Preserve

PROJECT DETAILS

Manager: Fred Cartwright
Number: 400127-29
Overall Budget: \$400,000

TIMELINE

Planning/Scoping: March 2023
Engineering/Design: March 2023
Procurement: March 2023
Construction: December 2023
Closeout: September 2024
Projected Completion Date: December 2024
Project Duration: 21 Months

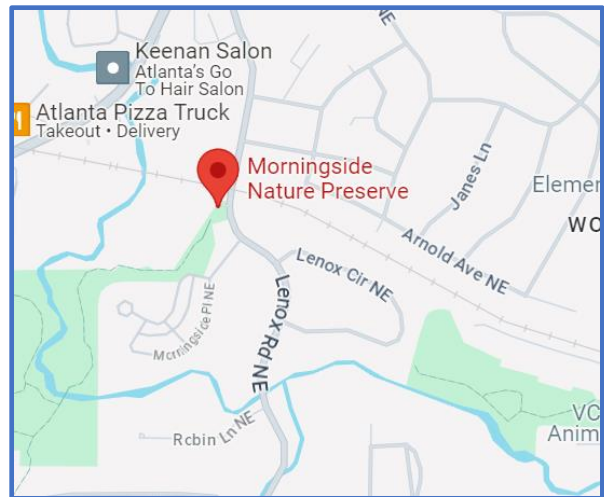

ENCUMBERED FUNDING

FUND	FY23	FY24	FY25
3163-MAF Social Bond 2022-A1	\$364,069		
