

OCTOBER 27, 2022

PROJECT UPDATE




Dekalb Avenue/Krog Street Safety and Drainage Improvements

Project Descriptions

The City of Atlanta's Departments of Transportation and Watershed Management are working to deliver safety and drainage improvements in the Dekalb Avenue corridor and Krog Street Tunnel. Crews are continuing the drainage improvement work in the Krog Street Tunnel. The contractor has advised of a possible delay for the full resurfacing based on personnel availability and the approaching winter temperatures. The City is working with the contractor on a revised schedule.

Locations

- ⇒ Dekalb Avenue NE (Decatur Street SE) from Jackson Street SE to Ridgcrest Road NE (Atlanta City Limit)
- ⇒ Krog Street NE/Dekalb Avenue NE intersection
- ⇒ Dekalb Avenue NE from Waddell Street NE to Cornelia Street SE
- ⇒ Krog Street from Dekalb Avenue and Edgewood Avenue NE

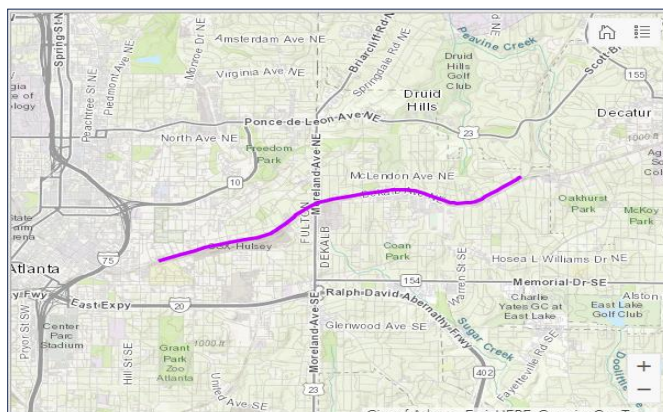

Schedules

- ⇒ Target completion for the Dekalb Avenue Safety Improvements project is Fall 2023.
- ⇒ Krog Street Stormwater Drainage - Phase I is underway, with a projected completion in Fall 2022.
- ⇒ Krog Street Stormwater Drainage - Phase II will begin upon completion of Phase I, with target completion date of Spring 2023.



Other Details

- ⇒ Department of Watershed Management (DWM) crews have begun work on the Krog Street Stormwater Drainage-Phase I project to restore the drainage system and mitigate flooding in the Krog Street Tunnel.
- ⇒ Krog Street Tunnel from Dekalb Avenue NE to Wylie Street SE will be closed nightly from 7 p.m. to 6 a.m., Sunday-Friday, until December 2022 to accommodate the construction at the Krog Street NE/Dekalb Avenue NE intersection.
- ⇒ One sidewalk within the Krog Street Tunnel, will remain open during the project. However, some construction activity (i.e., work that requires heavy equipment to install storm pipes, etc.) will require restricted sidewalk access on both sides.
- ⇒ Resurfacing of Dekalb Avenue NE (Decatur Street SE) from Jackson Street SE to Ridgcrest Road SE (Atlanta City Limits) will follow necessary infrastructure improvements. Utility relocation work is scheduled to be completed Winter 2022.
- ⇒ Adjustment of manhole covers and inlets continues.

Other Details (Continued)

- ⇒ To date:
 - ⇒ The Krog Street Tunnel lighting installation is complete.
 - ⇒ Crews have successfully repaired all damaged sidewalk.
 - ⇒ Missing sidewalk has been installed.
 - ⇒ Most of the non-compliant ADA ramps and driveway aprons have been brought to compliance, with one remaining.
 - ⇒ Eighty percent of the signal upgrades, including detection and radar, have been installed within the project limits.
 - ⇒ New street name signs have been installed.
 - ⇒ Watermains have been replaced from Dekalb Place to Oxford Place and from Moreland Avenue to Ferguson Street.
- ⇒ The remaining signal upgrades, pedestrian safety improvements, and removal of the reversible lane infrastructure will be completed after resurfacing is concluded.
- ⇒ Information about Krog Street closure to accommodate work at the Krog Street NE/Dekalb Avenue NE intersection is available at the ATLDOT website at: <https://atldot.atlantaga.gov/news-events>.
- ⇒ Information about the Dekalb Avenue Safety Improvements and the DWM Krog Street Stormwater Drainage-Phase I projects is available on the ATLDOT website at atldot.atlantaga.gov/projects/dekalb-ave-safety-improvements and the DWM website at: <https://www.atlantawatershed.org/dwm-projects/> and <https://cleanwateratlanta.h2o4atl.com/>.
- ⇒ Stay engaged with ATLDOT and DWM on Twitter at [@ATLDOT](https://twitter.com/ATLDOT) and [@ATLWatershed](https://twitter.com/ATLWatershed). You can also visit the [ATLDOT Facebook](https://www.facebook.com/ATLDOT) page, Instagram channel [@ATL.DOT](https://www.instagram.com/ATL.DOT), and [Nextdoor](https://www.nextdoor.com) pages for more information.
