

December 2, 2022

PROJECT UPDATE




Cascade Avenue/Road Complete Street Phase I

Project Descriptions

The City of Atlanta's Departments of Transportation and Watershed Management are working to deliver corridor improvements along approximately two (2) miles of Cascade Road/Avenue. Planned improvements include milling, resurfacing, restriping, sidewalks, traffic communications corridor signal upgrades, bus stop enhancements, streetscapes, extended bike lanes, pedestrian safety improvements, and relocation of hydrants, water main lines, sidewalk meter boxes, and street valve box adjustments.

Locations

- ⇒ Cascade Road/Avenue SW from the City Limits to Willis Mill Road SW and Delowe Drive SW to Avon Avenue SW
- ⇒ Water line relocation from Cascade Avenue SW/Clearbrook Drive SW intersection to the Cascade Road SW/Pollard Drive SW intersection

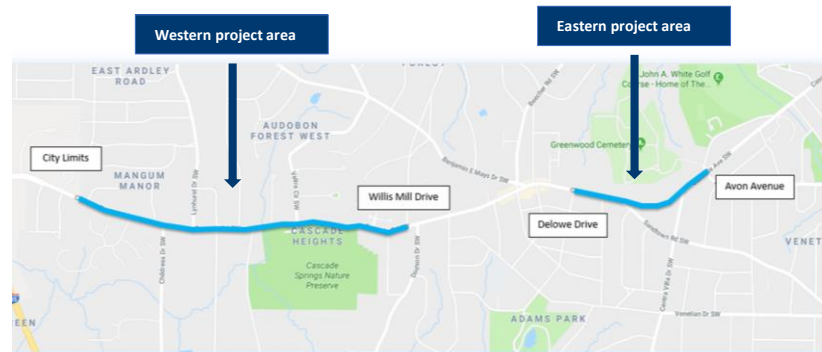

Schedules

- ⇒ Target completion for the Cascade Road/Avenue Complete Street Phase I roadway improvements is Spring 2025.

Other Details

- ⇒ DWM will relocate three hydrants in Summer 2023, completing all required waterline work.
- ⇒ There may be water service disruptions associated with the DWM relocation work. Impacted property owners will be notified (i.e., robocall, door knock, door hanger, etc.) prior to anticipated disruptions.
- ⇒ Five of the 11 utility companies have initiated relocation work on the eastern side of this project:
 - Atlanta Gaslight
 - Bandwidth IG
 - Comcast
 - Department of Watershed Manager
 - Google Fiber
- ⇒ Six remaining utility companies required to relocate include:
 - AT&T
 - GPC (Power)
 - GPC (Lighting)
 - TCA
 - Verizon
 - Zayo
- ⇒ Start and completion windows for additional utility relocations will be dependent on each company's relocation work. Utility companies' current projections are for completion by the end of 2023.

Other Details (Continued)

- ⇒ All utility relocations (water, gas, cable, telecommunications, etc.) must be transferred before the installation of “complete street” elements.
- ⇒ Project staged to begin “complete street” installations as relocations are completed in each of the two (2) construction areas:
 - Eastern side (Avon Avenue to Delowe Drive)
 - Western side (City Limits/Kingsdale Drive to Willis Mill Road) ⇒ Resurfacing of approximately 4.25 miles of Cascade Road/Avenue from the City Limits just west of Kingsdale Drive to Ralph David Abernathy Boulevard will take place upon completion of all other construction activities.
- ⇒ To Date:
 - DWM has completed 95% of its scheduled relocations. This includes:
 - The realignment of 12 water lines.
 - The relocation of two of five fire hydrants and the addition of one fire hydrant.

Information about the Cascade Road/Avenue Complete Street project is available on the ATLDOT website at: <https://atldot.atlantaga.gov/projects/cascade-rd-complete-street-ph-i> and the DWM website at: <https://www.atlantawatershed.org/dwm-projects/> and <https://cleanwateratlanta.h2o4atl.com/>.

- ⇒ Stay engaged with ATLDOT and DWM on Twitter at [@ATLDOT](https://twitter.com/ATLDOT) and [@ATLWatershed](https://twitter.com/ATLWatershed). You can also visit the [ATLDOT Facebook](https://www.facebook.com/ATLDOT) page, Instagram channel [@ATL.DOT](https://www.instagram.com/ATL.DOT), and [Nextdoor](https://www.nextdoor.com) pages for more information.
